



Activity ID	Activity Name	Duration	Start	Finish	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042							
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q				
Blackwater Gold Project		48.3y	31-Mar-23	02-Nov-70																												
	1 - Major Milestones	48.3y	31-Mar-23	02-Nov-70																												
	2 - Construction Schedule	3.2y	31-Mar-23	30-May-26																												
	3 - Year +1 to Year +5	5.7y	18-Oct-24	28-May-30																												
	4 - Year +6 to Year +10	5.1y	01-May-30	10-May-35																												
	5 - Year +11 to Year +18	11.0y	10-May-35	13-Mar-46																												
	6 - Year +19 to Year +23	5.0y	29-Mar-43	02-Mar-48																												
	7 - Year +24 to Year +45	22.0y	02-Mar-48	07-Nov-69																												
	8 - Post Closure Year +46	1.0y	07-Nov-69	02-Nov-70																												



Blackwater Gold Project

0 - Phase Roll Up

Printed: 17-Aug-26 at 08:54

Page 2 of 2

[illegible]

Activity Duration Activity Duration summary	TASK filter: All Activities	Date	Revision	Checked	Approved
17-Aug-26		V.009: Prepared pursuant to:	BW	RT/SEB	
		Blackwater Decision Statement condition 11.2			



Blackwater Gold Project


1 - Milestones

Printed: 17-Aug-26 at 08:55

Page 1 of 2

[illegible]

Activity Duration Activity Duration ◆ Milestone summary	TASK filter: WBS .	<table> <tr> <th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr> <tr> <td>17-Aug-26</td><td>V.009: Prepared pursuant to:</td><td>BW</td><td>RT/SEB</td></tr> <tr> <td></td><td>Blackwater Decision Statement condition 11.2</td><td></td><td></td></tr> <tr> <td></td><td></td><td></td><td></td></tr> <tr> <td></td><td></td><td></td><td></td></tr> </table>	Date	Revision	Checked	Approved	17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB		Blackwater Decision Statement condition 11.2										
Date	Revision	Checked	Approved																			
17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB																			
	Blackwater Decision Statement condition 11.2																					

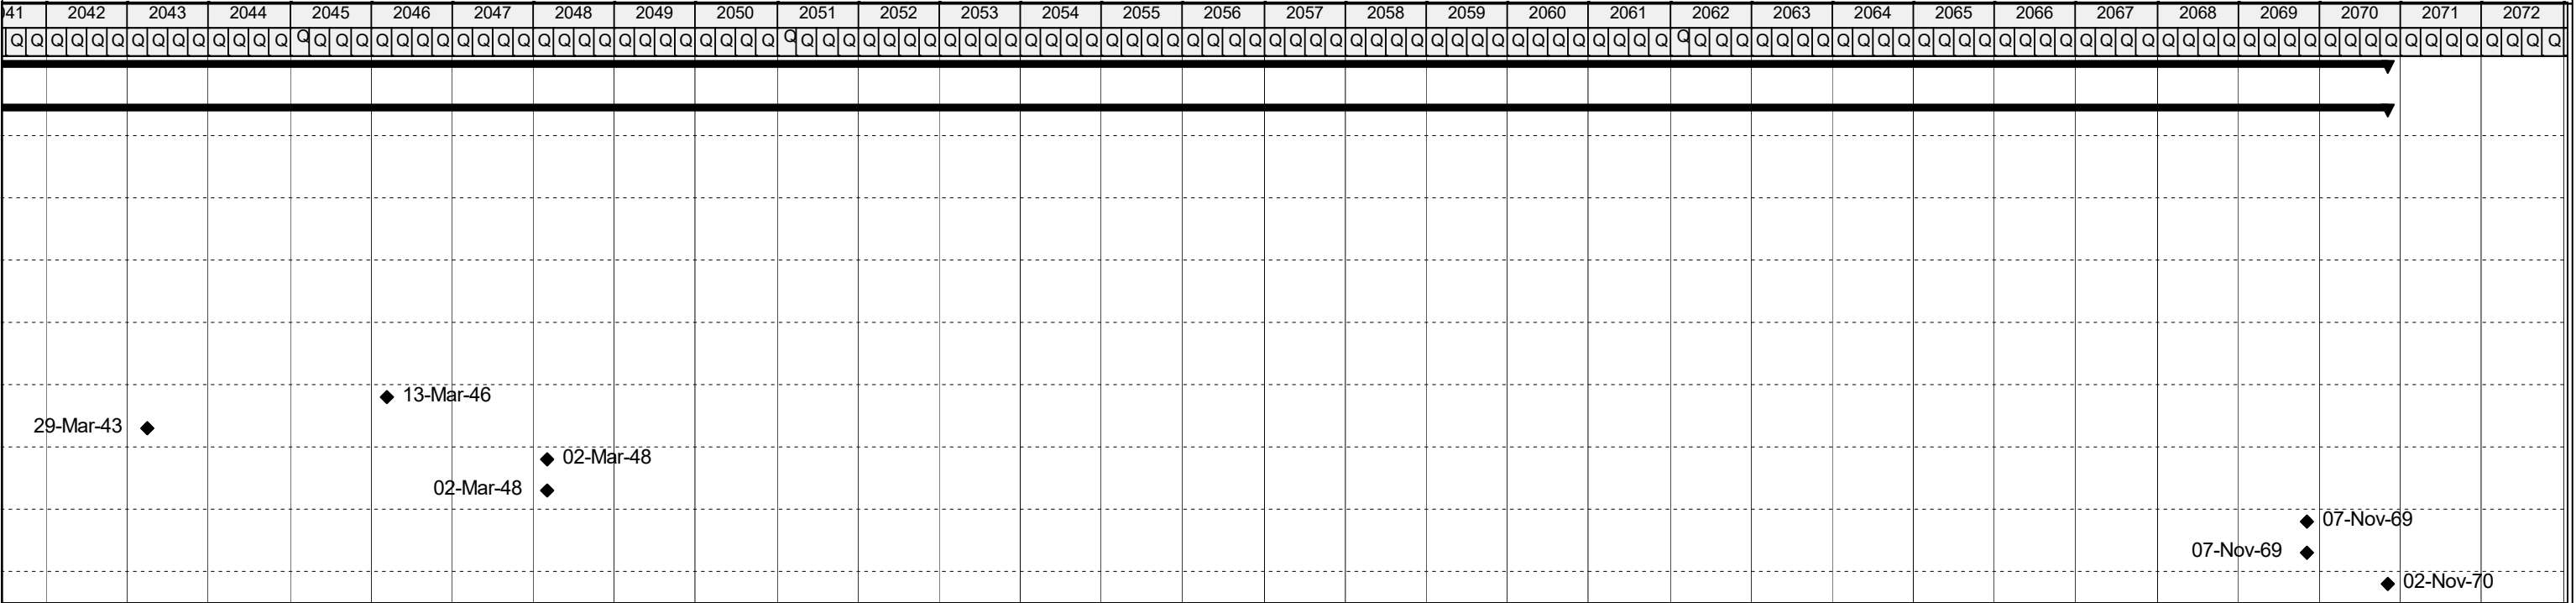

 Activity Duration  Activity Duration  summary	TASK filter: WBS .	Date	Revision	Checked	Approved
		17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
			Blackwater Decision Statement condition 11.2		

Activity Duration
Activity Duration
summary

 Activity Duration  Activity Duration  summary	TASK filter: WBS .	Date	Revision	Checked	Approved
		17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
			Blackwater Decision Statement condition 11.2		

 Activity Duration  Activity Duration  summary	TASK filter: Year 1 to 5.	Date	Revision	Checked	Approved
		17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
			Blackwater Decision Statement condition 11.2		



Blackwater Gold Project
3 - Year +1 to Year +5

Activity ID		Activity Name	Duration	Start	Finish	2024				2025				2026				2027				2028				2029				2030				2031		
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1		
		A2430	Final ECD – Construction and operation of dam and pond starting in Year +3; Pumpback of water to the TSF	2.2y	28-Feb-27	26-Apr-29										28-Feb-27																				
		Waste Stockpiles (WSF)			3.0y	07-May-27	21-Apr-30																													
		A1940	Vegetation clearing, grubbing, and surface preparation as required	3.0y	07-May-27	21-Apr-30											07-May-27																			
		A1945	Construction of Lower WSF water mgmt systems, including water collection channels & the Lower WSF Collection Pond	3.0y	07-May-27	21-Apr-30											07-May-27																			
		A1950	Lower Waste Stockpile – Stockpiling to 1,420 masl (Year +5)	3.0y	07-May-27	21-Apr-30											07-May-27																			
		Low Grade Ore (LGO) Stockpiles			5.0y	17-May-25	21-Apr-30																													
		A1960	Vegetation clearing, grubbing, and surface preparation as required	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A1970	Stockpiling of LGO Stockpile (lower grade ore) to lift height 1,500 masl (Year +3)	1.0y	07-May-27	01-May-28											07-May-27					01-May-28														
		Water Management Structures			5.0y	17-May-25	21-Apr-30																													
		A1990	Open Pit dewatering	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A2000	WMP outflows pumped to Processing Plant and FWR or discharge to environment	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A2510	Northern Diversion System const, collection channels, water transfer pond, intake structure and pipeline to FWR	0.6y	04-Jun-26	21-Jan-27											04-Jun-26					21-Jan-27														
		Water Treatment			5.0y	30-Jun-25	28-May-30																													
		A2010	Neutralization of Low Grade Ore (LGO) Stockpile runoff with lime before discharging to the TSF C Pond along with tailing	5.0y	30-Jun-25	28-May-30					30-Jun-25																									
		A2020	Treatment of water collecting in Open Pit & runoff from Lower Waste Stockpile treated by Metals WTP, if not going Plant	5.0y	30-Jun-25	28-May-30					30-Jun-25																									
		A2030	Treated water is used at the mill and excess treated water conveyed to WMP	5.0y	30-Jun-25	28-May-30					30-Jun-25																									
		A2040	Excess TSF C Pond water treatment at Reverse Osmosis WTP and discharge to the WMP	3.8y	01-Sep-26	28-May-30											01-Sep-26																			
		Mine Service and Haul Roads			5.0y	17-May-25	21-Apr-30																													
		A2050	Ex-pit haul roads – Expansion to service development of the pit	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A2060	In-pit haul roads – Expansion to service development of the pit	5.0y	17-May-25	21-Apr-30					17-May-25																									
		Mine Access Road (MAR)			4.0y	30-May-26	21-Apr-30																													
		A1110	Tree clearing, bulk excavation and grading, surfacing and installation of bridges	4.0y	30-May-26	21-Apr-30											30-May-26																			
		Ready Line and Bulk Fuel Supply			1.0y	01-May-28	26-Apr-29																													
		A2070	Fuel storage expanded to 300,000 L (Year +4)	1.0y	01-May-28	26-Apr-29																	01-May-28													
		Ongoing Use and Maintenance			5.0y	17-May-25	21-Apr-30																													
		A2080	Topsoil stockpiles	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A2090	Central Diversion System, WMP, and FWR	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A2100	Surface drainage for infrastructure	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A2110	Mine service roads	5.0y	17-May-25	21-Apr-30					17-May-25																									
		A2120	Power supply and distribution	5.0y	17-May-25	21-Apr-30					17-May-25																									
A2130	Explosives storage facility	5.0y	17-May-25	21-Apr-30					17-May-25																											
A2140	Ancillary facilities	5.0y	17-May-25	21-Apr-30					17-May-25																											
A2150	Borrow pits and aggregate and concrete batch plants (Plant expansion)	5.0y	17-May-25	21-Apr-30					17-May-25																											

Activity Duration
 Activity Duration
 summary

TASK filter: Year 1 to 5.

Date	Revision	Checked	Approved
17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
	Blackwater Decision Statement condition 11.2		



Activity ID		Activity Name	Duration	Start	Finish	2024				2025				2026				2027				2028				2029				2030				2031					
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4		Q1				
		Off-Site Infrastructure		5.0y	17-May-25	21-Apr-30																																	
		A1690	Decommissioning of Exploration Access Road	1.0y	25-Feb-29	20-Feb-30													25-Feb-29								20-Feb-30												
		A2160	Transmission line	5.0y	17-May-25	21-Apr-30	17-May-25																								21-Apr-30								
		A2170	Airstrip and airstrip access road – Construction and connection to Mine Access Road (MAR)	2.9y	30-Jun-27	21-Apr-30									30-Jun-27																				21-Apr-30				
		A4120	Installation of Fresh Water Supply System (FWSS)	2.9y	30-Jun-27	21-Apr-30									30-Jun-27																				21-Apr-30				

 Activity Duration  Activity Duration  summary	TASK filter: Year 6 to 10.	Date	Revision	Checked	Approved
		17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
			Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2029			2030				2031				2032				2033				2034				2035				2036	
					Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	
A2410	Expansion of water reclaim systems from TSF C Pond coinciding with processing facility expansions (Year +10)	1.0y	15-May-34	10-May-35																15-May-34								10-May-35					
	Waste Stockpiles (WSF)		5.0y	28-May-30	02-May-35																												
	A2440	Vegetation clearing, grubbing, and surface preparation as required	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2450	Lower Waste Stockpile – Expansion to ultimate 1,470 masl (Year +8); completion of stockpiling (Year +10)	3.0y	17-May-32	02-May-35								17-May-32																02-May-35				
	A2460	Upper Waste Stockpile – Grubbing and site prep, foundation prep, and water management construction (Year +10)	1.0y	07-May-34	02-May-35																07-May-34								02-May-35				
	Low Grade Ore (LGO) Stockpile		5.0y	28-May-30	02-May-35																												
	A2470	Vegetation clearing, grubbing, and surface preparation, as required	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2480	Stockpiling of LGO Stockpile (lower grade ore) to lift height 1,520 masl (Year +8)	1.0y	17-May-32	12-May-33								17-May-32								12-May-33												
	A2490	Stockpiling of LGO Stockpile Pile A (higher grade ore) to lift height 1,480 masl (Year +8)	1.0y	17-May-32	12-May-33								17-May-32								12-May-33												
	Water Management Structures		5.0y	28-May-30	02-May-35																												
	A2500	Open Pit dewatering	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2520	Relocation of Central Diversion System infrastructure to Phase 2 positions to the WMP (Year +6)	1.0y	28-May-30	23-May-31	28-May-30			23-May-31																								
	Mine Service and Haul Roads		5.0y	28-May-30	02-May-35																												
	A2530	In-pit Haul Roads – Expansion to service pit expansion	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	Power Supply and Distribution		5.0y	28-May-30	02-May-35																												
	A2540	Expansion of power distribution network to Processing Plant for increased throughput	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2550	Expansion of power distribution network to Open Pit for addition of electric drilling and shovel extraction	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	Ready Line and Bulk Fuel Supply		1.0y	12-May-33	07-May-34																												
	A2560	Fuel storage expanded to 675,000 L (Year +9)	1.0y	12-May-33	07-May-34												12-May-33								07-May-34								
	Water Treatment		5.0y	28-May-30	02-May-35																												
	A2570	Neutralization of Low Grade Ore (LGO) Stockpile runoff with lime before discharging to the TSF C Pond along with tailing	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2580	Treatment of waters from the Open Pit and runoff from the Upper Lower Waste stockpiles treated at the Metals WTP	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2590	Treated water is used at the mill and excess treated water conveyed to WMP	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2600	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	Ongoing Use and Maintenance		5.0y	28-May-30	02-May-35																												
	A2610	Topsoil stockpiles erosion control and invasive plant management	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				
	A2620	Central and Northern Diversion systems and Central Water Transfer Pond North and South Interception trenches	5.0y	28-May-30	02-May-35	28-May-30																							02-May-35				

Activity Duration
 Activity Duration
 summary

TASK filter: Year 6 to 10.

Date	Revision	Checked	Approved
17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
	Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2029			2030				2031				2032				2033				2034				2035				2036
					Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
A2630	Pit dewatering	5.0y	28-May-30	02-May-35				28-May-30																								
	A2640	Fresh Water Reservoir (FWR)	5.0y	28-May-30	02-May-35				28-May-30																							
	A2650	Surface drainage for Infrastructure	5.0y	28-May-30	02-May-35				28-May-30																							
	A2660	Mine service roads	5.0y	28-May-30	02-May-35				28-May-30																							
	A2670	Ex-pit haul roads	5.0y	28-May-30	02-May-35				28-May-30																							
	A2680	Power supply and distribution to other mine site components	5.0y	28-May-30	02-May-35				28-May-30																							
	A2690	Explosives storage facility	5.0y	28-May-30	02-May-35				28-May-30																							
	A2700	Ancillary structures	5.0y	28-May-30	02-May-35				28-May-30																							
	A2710	Borrow pits and aggregate and concrete batch plant (Plant expansion)	5.0y	28-May-30	02-May-35				28-May-30																							
	Off-Site Infrastructure		5.0y	28-May-30	02-May-35																											
A2720	Transmission line	5.0y	28-May-30	02-May-35				28-May-30																								
	A2730	Freshwater supply system (FWSS) intake, pump stations and pipeline	5.0y	28-May-30	02-May-35				28-May-30																							
	A2740	Airstrip and airstrip access road	5.0y	28-May-30	02-May-35				28-May-30																							



Activity ID		Activity Name		Duration	Start	Finish	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042	2043	2044	2045	2046	2047
							Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Blackwater Gold Project				11.0y	10-May-35	13-Mar-46															
5 - Year +11 to Year +18				11.0y	10-May-35	13-Mar-46															
Open Pit				8.0y	10-May-35	29-Mar-43															
A2750	Extraction Method – Diesel drill and shovel, and electric drill and shovel	8.0y	10-May-35	29-Mar-43	10-May-35																
A2760	Staged decrease to in-pit mine fleet (Year +15, Year +16, Year +17, Year +18)	4.0y	19-Apr-39	29-Mar-43							19-Apr-39										
A2770	North Pushback 1 – Mining to pit bottom 1,260 masl bench (Year +11)	1.0y	10-May-35	04-May-36	10-May-35					04-May-36											
A2780	North Pushback 2 – Mining to pit bottom 1,140 masl bench (Year +14)	1.0y	24-Apr-38	19-Apr-39						24-Apr-38			19-Apr-39								
A2790	South Pushback – Mining to pit bottom 1,160 masl bench (Year +18)	1.0y	03-Apr-42	29-Mar-43											03-Apr-42						
Processing Plant				1.0y	10-May-35	04-May-36															
A2800	Phase 3 of plant commissioning and operations to 20 Mtpa (Year +11)	1.0y	10-May-35	04-May-36	10-May-35					04-May-36											
Tailings Storage Facility (TSF)				11.0y	10-May-35	13-Mar-46															
A2810	Main Dam C – Monitoring and annual raises to final elevation of 1,353 masl (Year +18)	8.0y	10-May-35	29-Mar-43	10-May-35																
A2820	West Dam – Monitoring and raised to final elevation of 1,353 masl (Year +12)	1.0y	04-May-36	29-Apr-37				04-May-36			29-Apr-37										
A2830	Saddle Dam – Initial const to 1,337 masl (Year +12) raise in two stages to final elev of 1,353 masl by Year +18)	7.0y	04-May-36	29-Mar-43				04-May-36													
A2840	TSF C Pond – Receipt of mine site drainage & Open Pit; Impoundment of tailings ends in approx Year +21	11.0y	10-May-35	13-Mar-46	10-May-35																13-Mar-46
A2850	TSF C Pond – Serves as process water source.	8.0y	10-May-35	29-Mar-43	10-May-35																
A2860	Main Dam D – Monitoring and annual raises to the ultimate build of 1,324 masl (Year +18)	7.5y	10-May-35	30-Sep-42	10-May-35																
A2870	TSF D Pond - Receipt of mine site drainage network, ECD Pond, & Open Pit until Year +19	9.0y	10-May-35	23-Mar-44	10-May-35																
A2880	TSF D Pond - Impoundment of PAG; Serves as process water source	9.0y	10-May-35	23-Mar-44	10-May-35																
A2890	ECD and Pond– Monitoring of dam and pond; Pumpback of water to the TSF D Pond	11.0y	10-May-35	13-Mar-46	10-May-35																13-Mar-46
Waste Stockpiles (WSF)				8.0y	10-May-35	29-Mar-43															
A2900	Lower Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	8.0y	10-May-35	29-Mar-43	10-May-35																
A2910	Upper Waste Stockpile – Expansion to 1,620 masl lift with cessation of stockpiling (Year +18)	1.0y	03-Apr-42	29-Mar-43											03-Apr-42						
Low Grade Ore (LGO) Stockpile				8.0y	10-May-35	29-Mar-43															
A2920	Vegetation clearing, grubbing, and surface preparation as required	8.0y	10-May-35	29-Mar-43	10-May-35																
A2930	Stockpiling of LGO Stockpile to lift height 1,540 masl (Year +13)	1.0y	29-Apr-37	24-Apr-38						29-Apr-37			24-Apr-38								
A2932	Stockpiling of LGO Stockpile to lift height 1,520 masl (Year +18)	1.0y	03-Apr-42	29-Mar-43											03-Apr-42						
A2940	Stockpiling of LGO Stockpile Pile A to lift height 1,480 masl (Year +13)	1.0y	29-Apr-37	24-Apr-38						29-Apr-37			24-Apr-38								
A2942	Stockpiling of LGO Stockpile Pile A height 1,480 masl, handling to commence in Year +15,	1.0y	19-Apr-39	13-Apr-40								19-Apr-39			13-Apr-40						

Activity Duration
 Activity Duration
 summary

TASK filter: Year 11 to 18.

Date	Revision	Checked	Approved
17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
	Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042	2043	2044	2045	2046	2047
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
A2950	Low Grade Ore (LGO) Stockpile Pile A will be depleted by Year +18	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
Water Treatment		8.0y	10-May-35	29-Mar-43															
A2960	Neutralization of Low Grade Ore (LGO) Stockpile runoff with lime before discharge along with tailings to TSF C	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A2970	Treatment of waters from the Open Pit and run off from the Upper and Lower Waste Stockpiles treated by Metals WTP	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A2980	Metals WTP treated water is used at the mill and excess treated water conveyed to WMP	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A2990	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP, if req'd due to prevailing climate condition	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
Water Management Structures		1.0y	04-May-36	29-Apr-37															
A3000	Water Management Pond relocated to accommodate continued filling of TSF C (Year +12)	1.0y	04-May-36	29-Apr-37			04-May-36		29-Apr-37										
Mine Service and Haul Roads		8.0y	10-May-35	29-Mar-43															
A3010	In-pit haul roads – Expansion to service pit expansion	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
Components Ongoing Use and Maintenance		8.0y	10-May-35	29-Mar-43															
A3020	Topsoil stockpiles	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3030	Central and Northern Diversion Systems	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3040	ECD, interception trenches, and pumpback system	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3050	FWR	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3060	Surface drainage for infrastructure	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3070	Mine service roads	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3080	Ex-pit haul roads	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3090	Power supply and distribution	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3100	Explosives storage facility	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3110	Ancillary facilities	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3120	Borrow pits and aggregate sources	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
Off-Site Infrastructure		8.0y	10-May-35	29-Mar-43															
A3130	Transmission line	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3140	FWSS pumphouse and pipeline	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				
A3150	Airstrip and airstrip access road	8.0y	10-May-35	29-Mar-43		10-May-35									29-Mar-43				

Activity Duration
 Activity Duration
 summary

TASK filter: Year 11 to 18.

Date	Revision	Checked	Approved
17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
	Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2042			2043				2044				2045				2046				2047				2048			
					Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Blackwater Gold Project		5.0y	29-Mar-43	02-Mar-48																											
6 - Year +19 to Year +23		5.0y	29-Mar-43	02-Mar-48																											
Open Pit		5.0y	29-Mar-43	02-Mar-48																											
A3160	Decommissioning of mine fleet and electrical distribution system, de-watering wells, sumps, and related works	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3170	Initiate filling of Pit Lake (See Water Management Structures)	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
Processing Plant		5.0y	29-Mar-43	02-Mar-48																											
A3180	Milling of Low Grade Ore (LGO) Stockpile reclaim at 20 Mt per annum (Year +19 to Year +22)3	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
Tailings Storage Facility (TSF)		5.0y	29-Mar-43	02-Mar-48																											
A3190	West Dam – Monitoring and maintenance	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3200	Main Dam C – Monitoring and maintenance of dam	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3210	TSF C Pond – Conveyance of supernatant to Open Pit starting Year +19; Serves as process water source;	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3220	TSF C Pond – tailings infill ceases Year +21	3.0y	29-Mar-43	13-Mar-46	29-Mar-43					13-Mar-46																					
A3230	Main Dam D – Monitoring and maintenance and raised to final elevation of 1,331 masl (Year +20)	1.0y	23-Mar-44	18-Mar-45				23-Mar-44		18-Mar-45																					
A3240	TSF D Pond – Receipt from mine site drainage network; impoundment of PAG, impoundment of tailings starting in Year +21	3.0y	18-Mar-45	02-Mar-48				18-Mar-45																		02-Mar-48					
A3250	TSF D Pond – serves as process water source	3.0y	18-Mar-45	02-Mar-48				18-Mar-45																		02-Mar-48					
A3260	ECD and Pond – Monitoring of dam and pond; Conveyance of captured flows to Open Pit starting Year +19	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
Waste Stockpiles (WSF)		5.0y	29-Mar-43	02-Mar-48																											
A3270	Lower Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3280	Upper Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
Low Grade Ore (LGO) Stockpile		5.0y	29-Mar-43	02-Mar-48																											
A3290	Re-handling of ore to Processing Plant with depletion by Year +23	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3300	Closure and progressive reclamation	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
Water Management Structures		5.0y	29-Mar-43	02-Mar-48																											
A3310	Pit Lake – Filling with natural groundwater and TSF C Pond supernatant (Year +20 to Year +23), and ECD Pond	4.0y	23-Mar-44	02-Mar-48				23-Mar-44																		02-Mar-48					
A3320	Lower Waste Stockpile runoff directed to TSF C Pond and Upper Waste Stockpile runoff directed to Open Pit	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3330	Continued operation of FWR for mill processing supply and Davidson Creek instream flow needs (IFN)	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
A3340	Continued operation of the Central and Northern Diversion Systems with water conveyed to the WMP and FWR, respectively	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																					02-Mar-48					
Water Treatment		5.0y	29-Mar-43	02-Mar-48																											

Activity Duration

Activity Duration

summary

TASK filter: Year 19 to 23.

Date

17-Aug-26

Revision

V.009: Prepared pursuant to:
Blackwater Decision Statement condition 11.2

Checked

BW

Approved

RT/SEB



Activity ID	Activity Name	Duration	Start	Finish	2042			2043				2044				2045				2046				2047				2048			
					Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
A	A3350	Continued operation of the lime neutralization for Low Grade Ore (LGO) Stockpile runoff	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3360	Metals treatment for pit dewatering, the Upper and Lower Waste Stockpiles not required.	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3370	Pit water will be allowed to naturally flow into the Open Pit to aid in pit filling.	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3380	Lower WSP water will be directed to the TSF; Upper WSP water will be directed to the Open Pit and TSF.	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3390	Membrane treatment of excess TSF C water not required as it will be pumped to the Open Pit to aid in pit filling	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	Mine Service and Haul Roads		5.0y	29-Mar-43	02-Mar-48																										
	A3400	Ex-pit haul roads – Progressive closure and reclamation	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3410	In-pit haul roads – Closure and progressive inundation of in-pit haul roads (Year +19)	1.0y	29-Mar-43	23-Mar-44	29-Mar-43	23-Mar-44																02-Mar-48								
	Power Supply and Distribution		5.0y	29-Mar-43	02-Mar-48																										
	A3420	Decommissioning of electrical distribution to Open Pit for drills and shovels	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	Explosives Storage Facility		5.0y	29-Mar-43	02-Mar-48																										
	A3430	Progressive closure and reclamation	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	Components Ongoing Use and Maintenance		5.0y	29-Mar-43	02-Mar-48																										
	A3440	Topsoil stockpiles	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3450	Central and Northern Diversion Systems	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3460	ECD, interception trenches, and pumpback system	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3470	FWR Surface drainage for infrastructure	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3480	Mine service roads	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3490	Power supply and distribution	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3500	Ancillary facilities	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3510	Borrow pits and aggregate sources	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	Off-Site Infrastructure		5.0y	29-Mar-43	02-Mar-48																										
	A3520	Transmission Line	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3530	FWSS pumphouse and pipeline	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								
	A3540	Airstrip and airstrip access road	5.0y	29-Mar-43	02-Mar-48	29-Mar-43																	02-Mar-48								



Activity ID	Activity Name	Duration	Start	Finish	2047				2048				2049				2050				2051				2052				2053				2054							
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
Blackwater Gold Project					22.0y				02-Mar-48				07-Nov-69																											
7 - Year +24 to Year +45					22.0y				02-Mar-48				07-Nov-69																											
Open Pit					22.0y				02-Mar-48				07-Nov-69																											
A3550	Filling of Pit Lake to be completed (Year +45)	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
Processing Plant					22.0y				02-Mar-48				07-Nov-69																											
A3560	Decommissioning (Year +24 and Year +25)	2.0y	02-Mar-48	20-Feb-50	02-Mar-48								20-Feb-50																											
A3562	Reclamation (Year +26 onwards)	20.0y	20-Feb-50	07-Nov-69									20-Feb-50																											
Tailings Storage Facility (TSF)					22.0y				02-Mar-48				07-Nov-69																											
A3570	Reclamation of dams/tailings beaches	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
Waste Stockpiles (WSF)					22.0y				02-Mar-48				07-Nov-69																											
A3580	Lower Waste Stockpile – Rehandling material for reclamation purposes followed by reclamation and monitoring	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
A3590	Upper Waste Stockpile – Reclamation followed by monitoring	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
Low Grade Ore (LGO) Stockpile					22.0y				02-Mar-48				07-Nov-69																											
A3600	Reclaimed with monitoring and maintenance as required	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
Topsoil Stockpiles					1.0y				20-Feb-50				15-Feb-51																											
A3610	Handling and distribution of salvaged soil with eventual closure and reclamation of the stockpiles (Year +26)	1.0y	20-Feb-50	15-Feb-51									20-Feb-50				15-Feb-51																							
Mine Service and Haul Roads					22.0y				02-Mar-48				07-Nov-69																											
A3620	Operation and maintenance of roads needed for the Closure phase	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
A3630	Decommissioning and reclamation of other roads	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
Power Supply and Distribution					22.0y				02-Mar-48				07-Nov-69																											
A3640	Operation and maintenance of power supply and distribution needed for the Closure phase	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
A3650	Decommissioning and reclamation of other components of the power supply	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																																			
Ancillary Structures					20.0y				20-Feb-50				07-Nov-69																											
A3660	Helipad – Decommissioning and reclamation (Year +25)	1.0y	20-Feb-50	15-Feb-51									20-Feb-50				15-Feb-51																							
A3670	Camp Facilities – Decommissioning and reclamation (Year +26)	1.0y	15-Feb-51	10-Feb-52													15-Feb-51				10-Feb-52																			
A3680	Construction Laydown Areas – Decommissioning and reclamation (Year +26)	1.0y	15-Feb-51	10-Feb-52													15-Feb-51				10-Feb-52																			
A3690	Truck shop/Mine office – Modification for vehicle servicing, fuel storage and dispensing, for Closure Phases (Year +26)	1.0y	15-Feb-51	10-Feb-52													15-Feb-51				10-Feb-52																			
A3700	Mine site shop, warehousing, offices and accommodations for Closure Phases (Year +26)	1.0y	15-Feb-51	10-Feb-52													15-Feb-51				10-Feb-52																			
A3710	Ready Line and Bulk Fuel Storage area – Decommissioning and reclamation (Year +26)	1.0y	15-Feb-51	10-Feb-52													15-Feb-51				10-Feb-52																			
A3720	Waste Management Facilities – Decommissioning and reclamation (Year +26)	1.0y	15-Feb-51	10-Feb-52													15-Feb-51				10-Feb-52																			



Blackwater Gold Project

7 - Year +24 to Year +45

[illegible]

 Activity Duration  Activity Duration  summary	TASK filter: WBS .	Date	Revision	Checked	Approved
		17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
			Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2047				2048				2049				2050				2051				2052				2053				2054				
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
	A3730	Potable and fire water supplies – Decommissioning and reclamation (Year +26)	1.0y	15-Feb-51	10-Feb-52													15-Feb-51								10-Feb-52											
	A3740	Communications – Decommissioning and reclamation (Year +27)	1.0y	10-Feb-52	04-Feb-53																	10-Feb-52								04-Feb-53							
	A3750	Security - Replace manned gatehouse with security gate and fencing (Year +27 to Year +44)	17.0y	04-Feb-53	07-Nov-69																					04-Feb-53											
	Borrow Pits, Aggregate Screening and Concrete Batch Plants		1.0y	10-Feb-52	04-Feb-53																																
	A3760	Decommissioning and reclamation (Year +27)	1.0y	10-Feb-52	04-Feb-53																	10-Feb-52								04-Feb-53							
	Off-Site Infrastructure		22.0y	02-Mar-48	07-Nov-69																																
	A3770	Airstrip and airstrip access road – Decommissioning and reclamation (Year +25)	1.0y	02-Mar-48	25-Feb-49	02-Mar-48								25-Feb-49																							
	A3790	Transmission Line – Operation and maint for water treatment plants at mine site then decommissioning and reclamation	22.0y	02-Mar-48	07-Nov-69	02-Mar-48																															
	A3780	FWSS pumphouse and pipeline – Decommissioning and reclamation (Year +45)	1.0y	12-Nov-68	07-Nov-69																																

TASK filter: WBS .

Date	Revision	Checked	Approved
17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
	Blackwater Decision Statement condition 11.2		



Blackwater Gold Project

7 - Year +24 to Year +45

[illegible]

 Activity Duration  Activity Duration  summary	TASK filter: WBS .	Date	Revision	Checked	Approved
		17-Aug-26	V.009: Prepared pursuant to:	BW	RT/SEB
			Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2070															
					Qtr 4				Qtr 1			Qtr 2			Qtr 3			Qtr 4		
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Blackwater Gold Project		1.0y	07-Nov-69	02-Nov-70																
8 - Post Closure Year +46		1.0y	07-Nov-69	02-Nov-70																
Open Pit		1.0y	07-Nov-69	02-Nov-70																
A3800	Open Pit pond level maintained at or below design maximum	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
Tailings Storage Facility (TSF)		1.0y	07-Nov-69	02-Nov-70																
A3810	Closed when water quality objectives met	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
A3820	Ongoing monitoring and reporting on stability of TSF dams	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
Water Treatment		1.0y	07-Nov-69	02-Nov-70																
A3830	Relocation of the Membrane WTP to a new facility adjacent to the ECD	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
A3840	Treated water from ECD, Pit Lake, and TSF C at the Membrane WTP prior to discharge to Davidson Creek	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
Mine Service and Haul Roads		1.0y	07-Nov-69	02-Nov-70																
A3850	Operation and maintenance of roads needed for the Post-closure phase	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
A3860	Decommissioning and reclamation of unused roads	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
Power Supply and Distribution		1.0y	07-Nov-69	02-Nov-70																
A3870	Operation and maintenance of power supply and distribution needed for the Post-closure phase	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
A3880	Decommissioning and reclamation of other components of the power supply	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
Security		1.0y	07-Nov-69	02-Nov-70																
A3890	Security gate access	1.0y	07-Nov-69	02-Nov-70	07-Nov-69														02-Nov-70	
